


6th & Main Lateral

Project Status Update 09-17-2021

Project Schedule

Design Notice to Proceed:	06-23-2021
Schematic (15%) Submittal:	08-09-2021
60% Design Submittal:	09-17-2021
90% Design Submittal:	
IFC Design Submittal:	

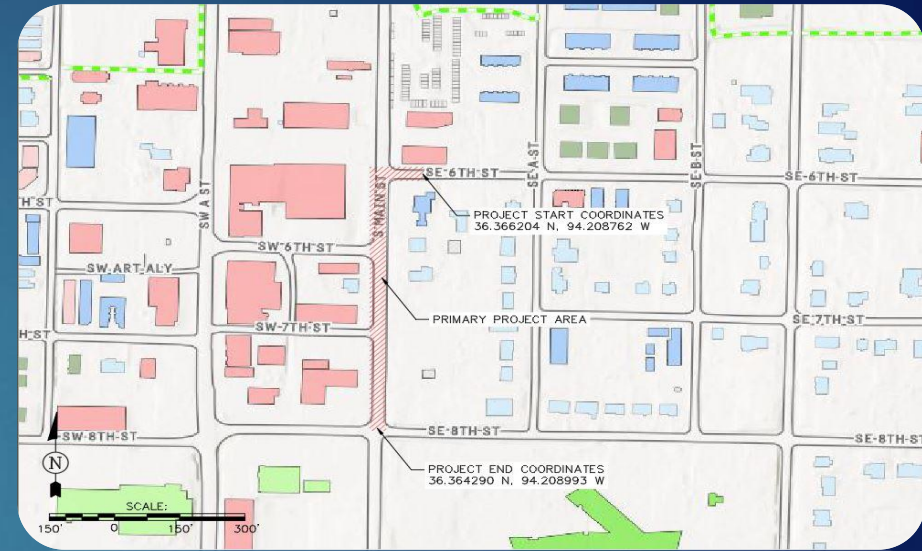

Notes

60% Design Submittal was uploaded to the AutoDesk file sharing site on Friday, September 17th.

Project Contacts

City of Bentonville: Dan Weese
Engineer: PMI
Contractor:

Action Items

- ❑ Confirm preferred curb inlet product number (Neenah Foundry R-3504-F grate inlets have been identified at several other new development sites)
- ❑ Discuss project scope related to other projects in the area. 8th Street Improvements currently show curb inlets and junction boxes added near the Main Street Intersection. Should PMI design tie into these systems or offer a different perspective for areas where systems overlap?
- ❑ Confirm preferred inlet box layout. Other designs show inlet boxes offset into the roadway. Should all boxes be constructed under the road surface to avoid other utilities in the project area?
