

SW 7th and C Lateral

Project Status Update 10/09/2021

Project Schedule


Design Notice to Proceed: 15/07/2021

Begin Survey Work: 27/08/2021

Survey Field Work Complete: 10/09/2021

50% Design Plans 22/09/2021

90% Design Plans 15/10/2021

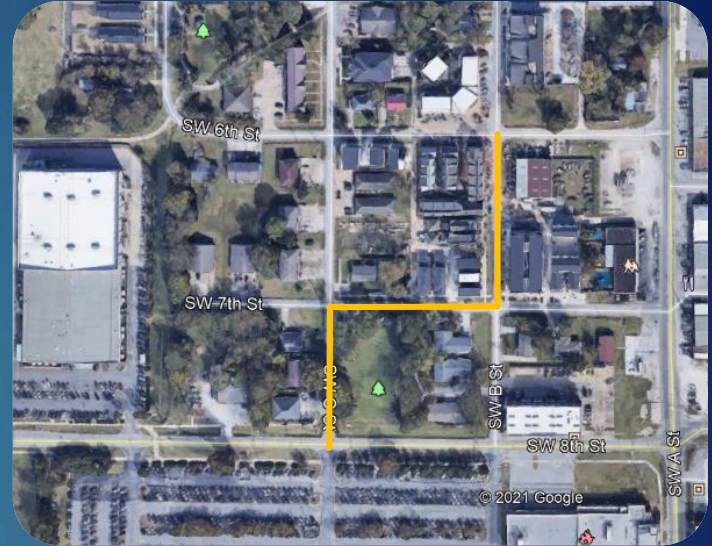

Notes

Most current notes from the previous week.

Project Contacts

City of Bentonville: Andrea Jobe, PE

Engineer: Daniel Ellis, PE

Engineer: Libby Topping

Contractor: TBD

Action Items

- 50% Design Plans to City 22/09/2021
- Public Hearing 28/09/2021
- 90% Design Plans to City 15/10/2021
